



Florida Department of
TRANSPORTATION

US 41 at Gulfstream Avenue Roundabout Construction Project



Financial Project ID: 438137-1-62-01

Project Overview

The purpose of this project is to replace the existing signalized intersection on US 41 at Gulfstream Avenue with a multi-lane roundabout to improve non-motorized connectivity and access, as well as vehicular traffic flow and operations, between the City of Sarasota's Downtown Central Business District (CBD), and the Bayfront area.

- Construction Start Date: March 15, 2021
- Construction Low-Bid Cost: \$8.6M
- Estimated Construction Completion: Fall 2022
- Contractor: Russell Engineering, Inc.


Project Improvements:

- ✓ Replace the signalized intersection on US 41 at Gulfstream Avenue with a multi-lane roundabout
- ✓ Install HAWK pedestrian crossing signal system, raised pedestrian refuge islands, new sidewalks and pedestrian walkways
- ✓ Replace underground drainage facilities, utilities, fiber optic communications, and LED streetlights
- ✓ Reconfigure stormwater retention ponds

Project Impacts:

- During construction, the speed limit will be reduced to **25 mph** on US 41 and Gulfstream Avenue
- Construction activities will take place during daytime hours, with occasional nighttime activities
- Detours and lane closures will be in place during various phases of the project


Traffic Movements / Pre-Phase

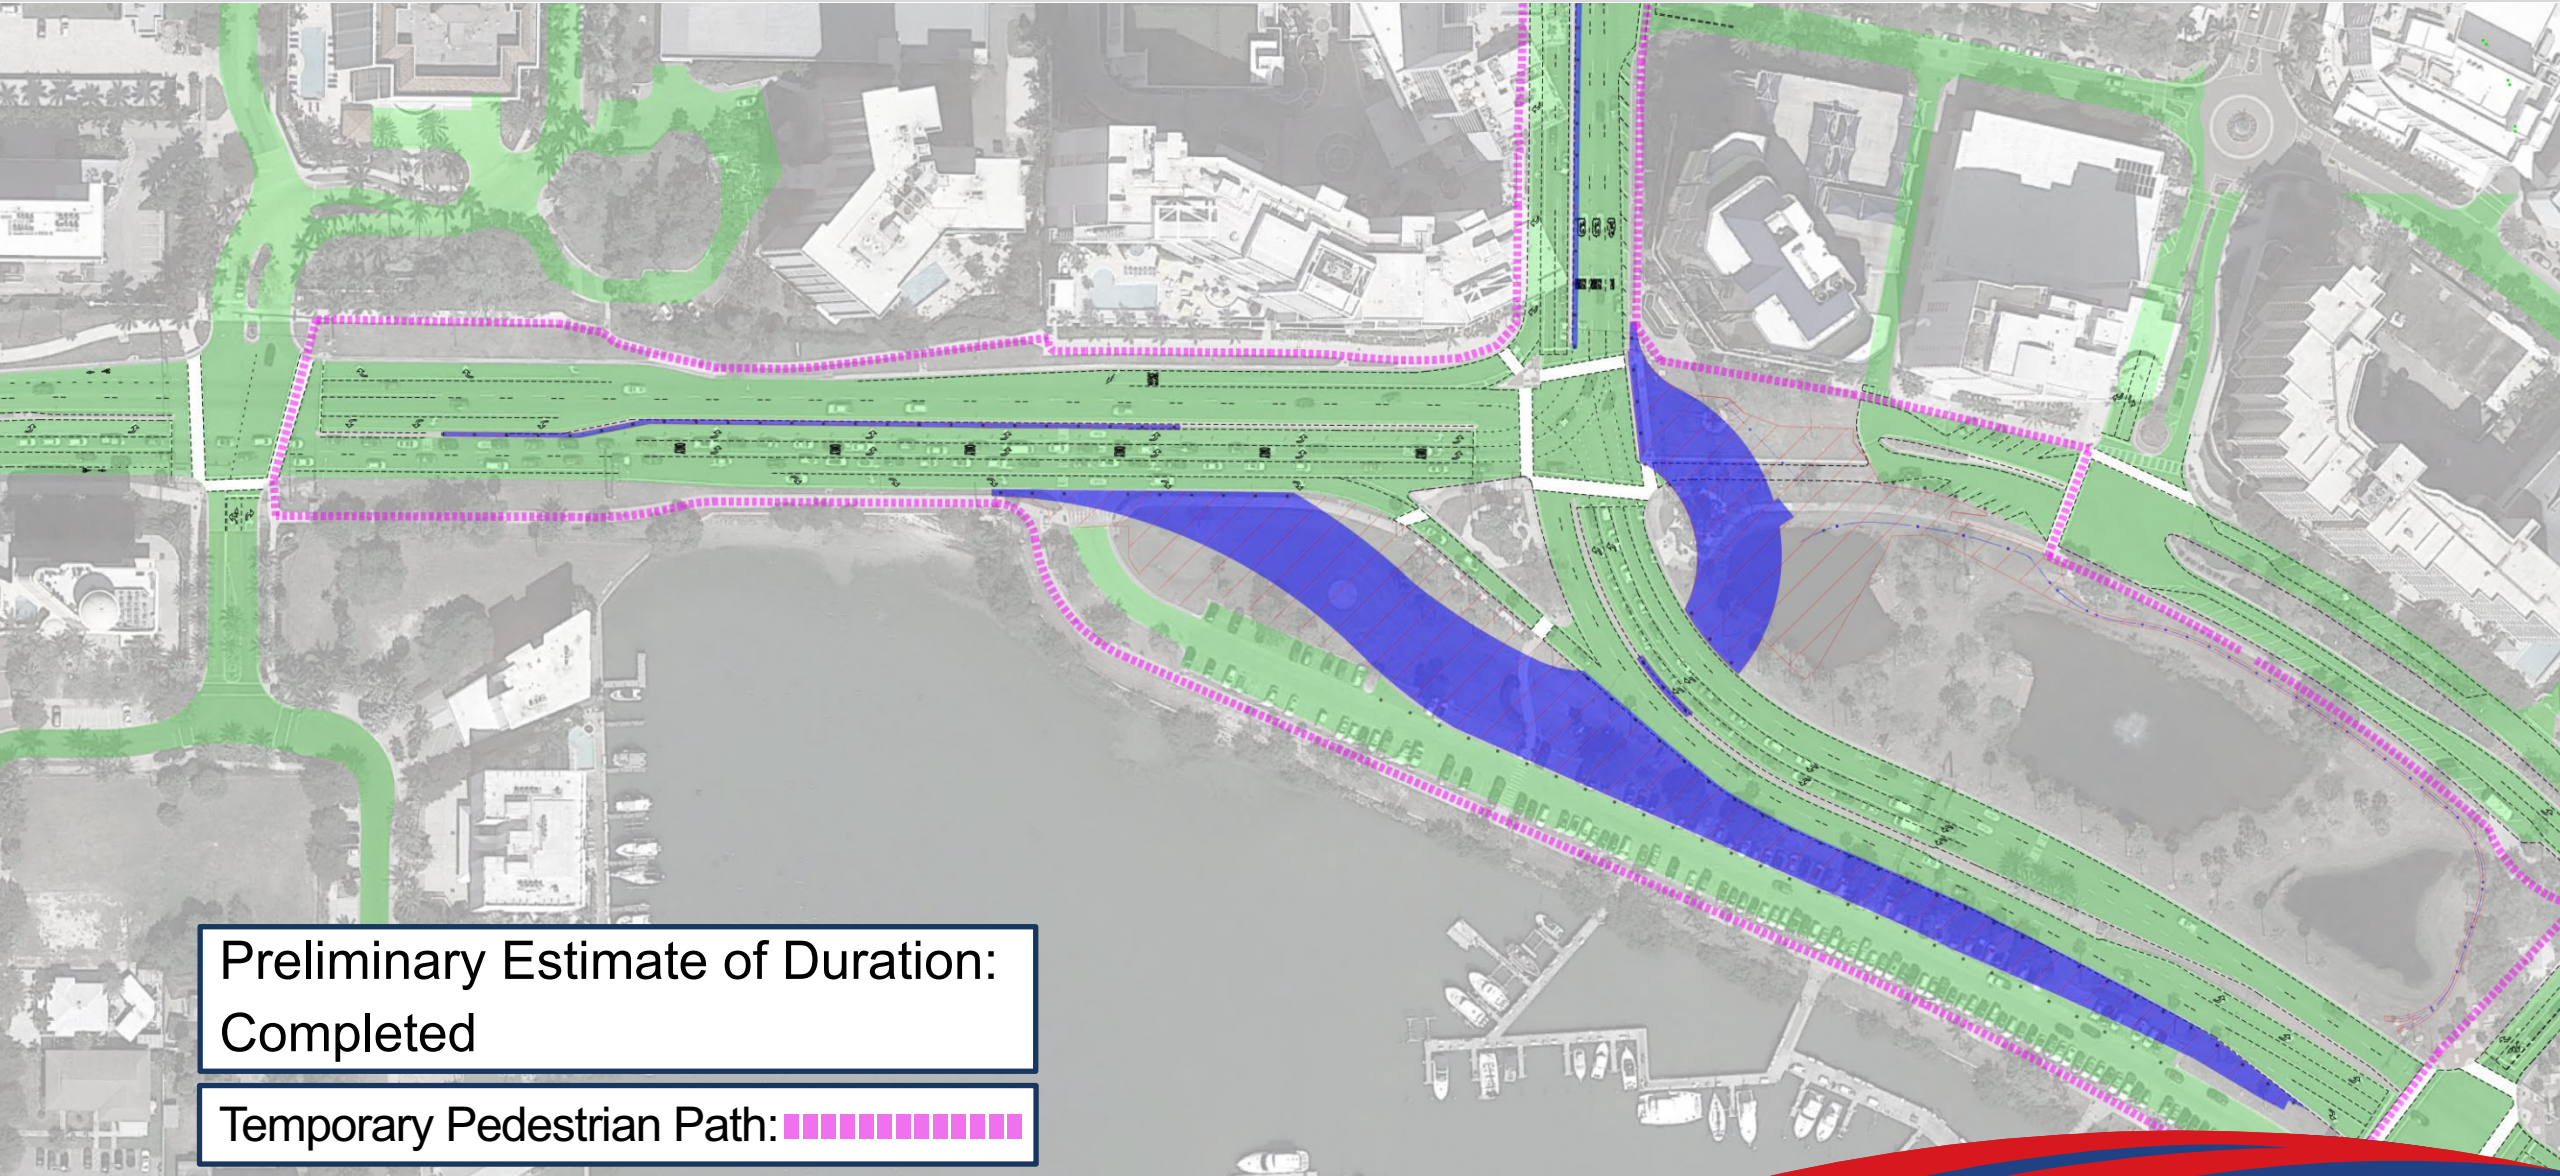

Preliminary Estimate of Duration:
Completed

Temporary Pedestrian Path: 


Traffic Movements / Phase IA

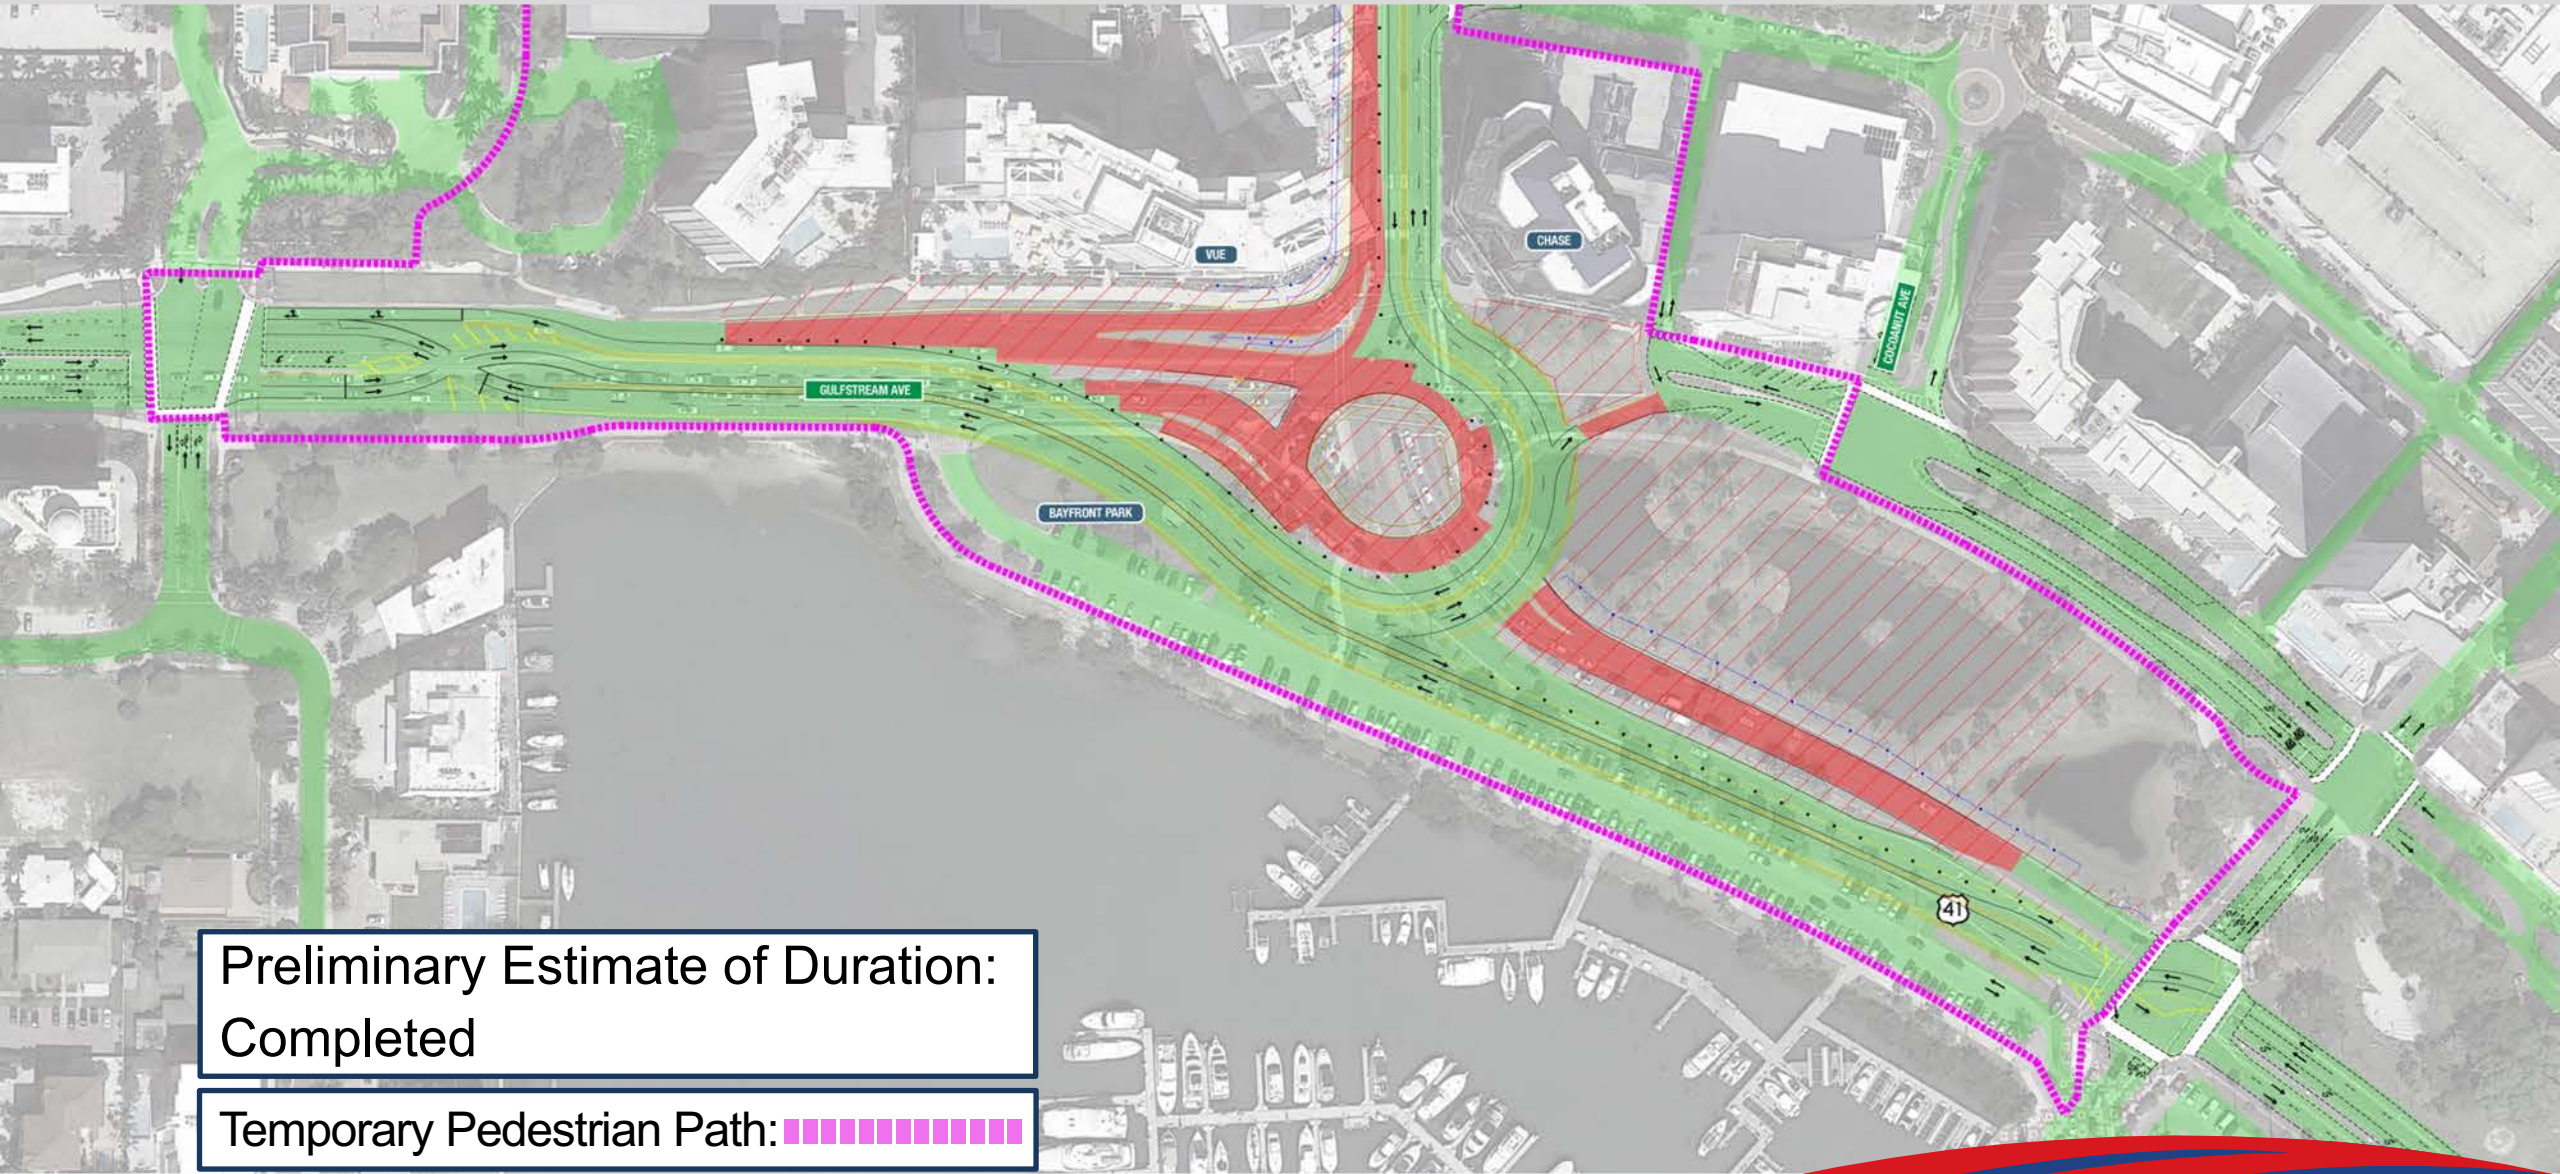

Preliminary Estimate of Duration:
Completed

Temporary Pedestrian Path: 


Traffic Movements / Phase IB

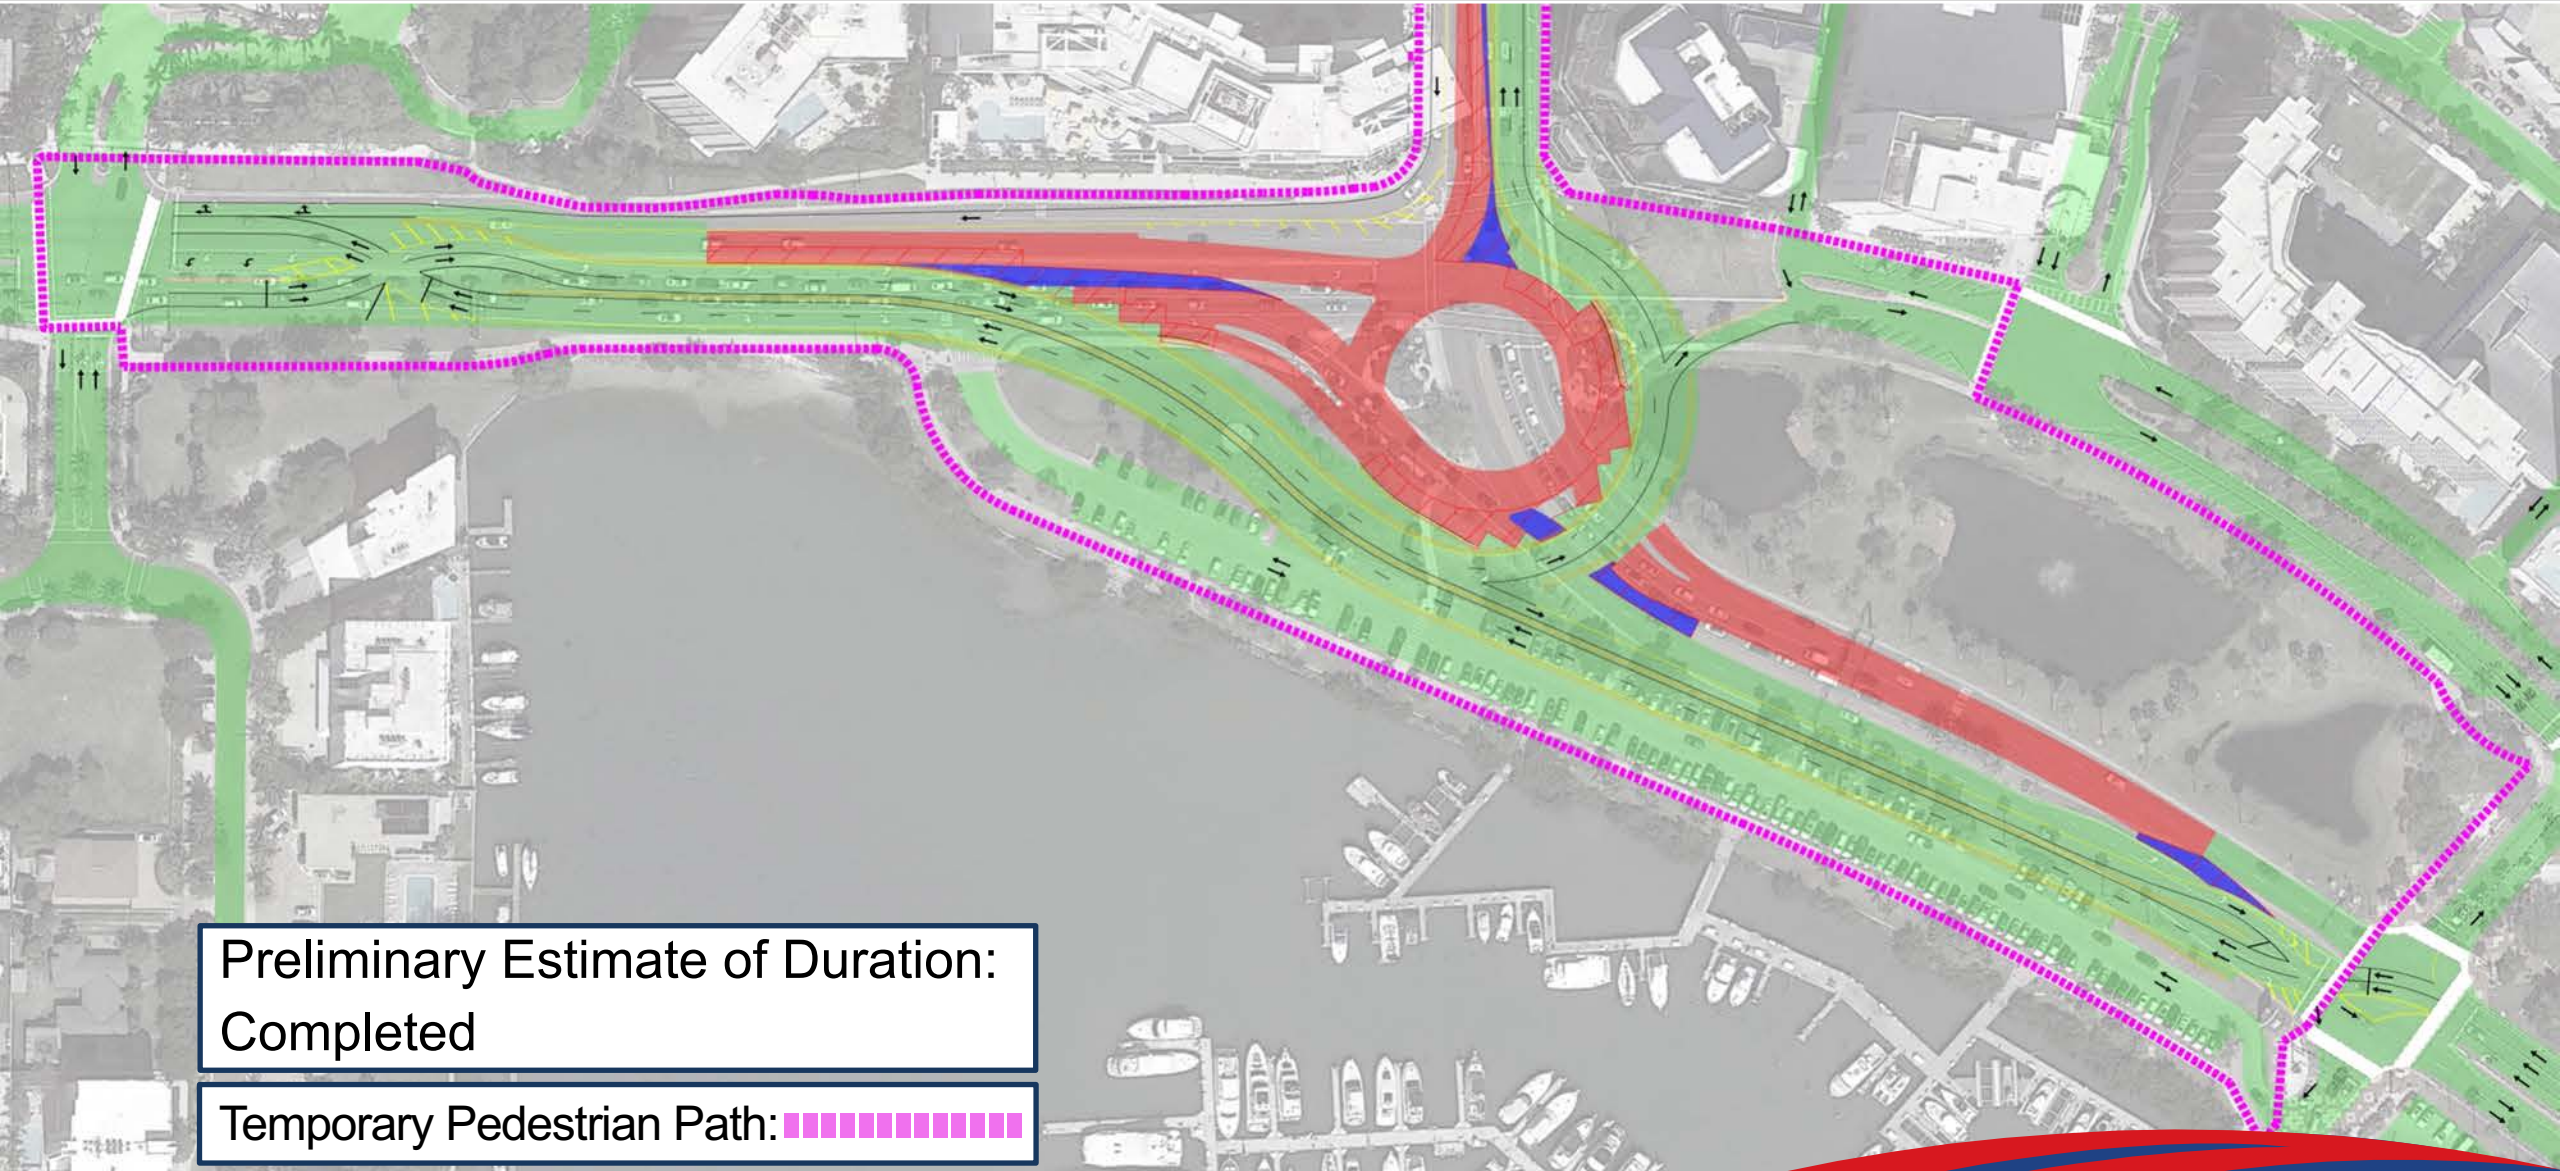

Preliminary Estimate of Duration:
Completed

Temporary Pedestrian Path: 


Traffic Movements / Phase IIA

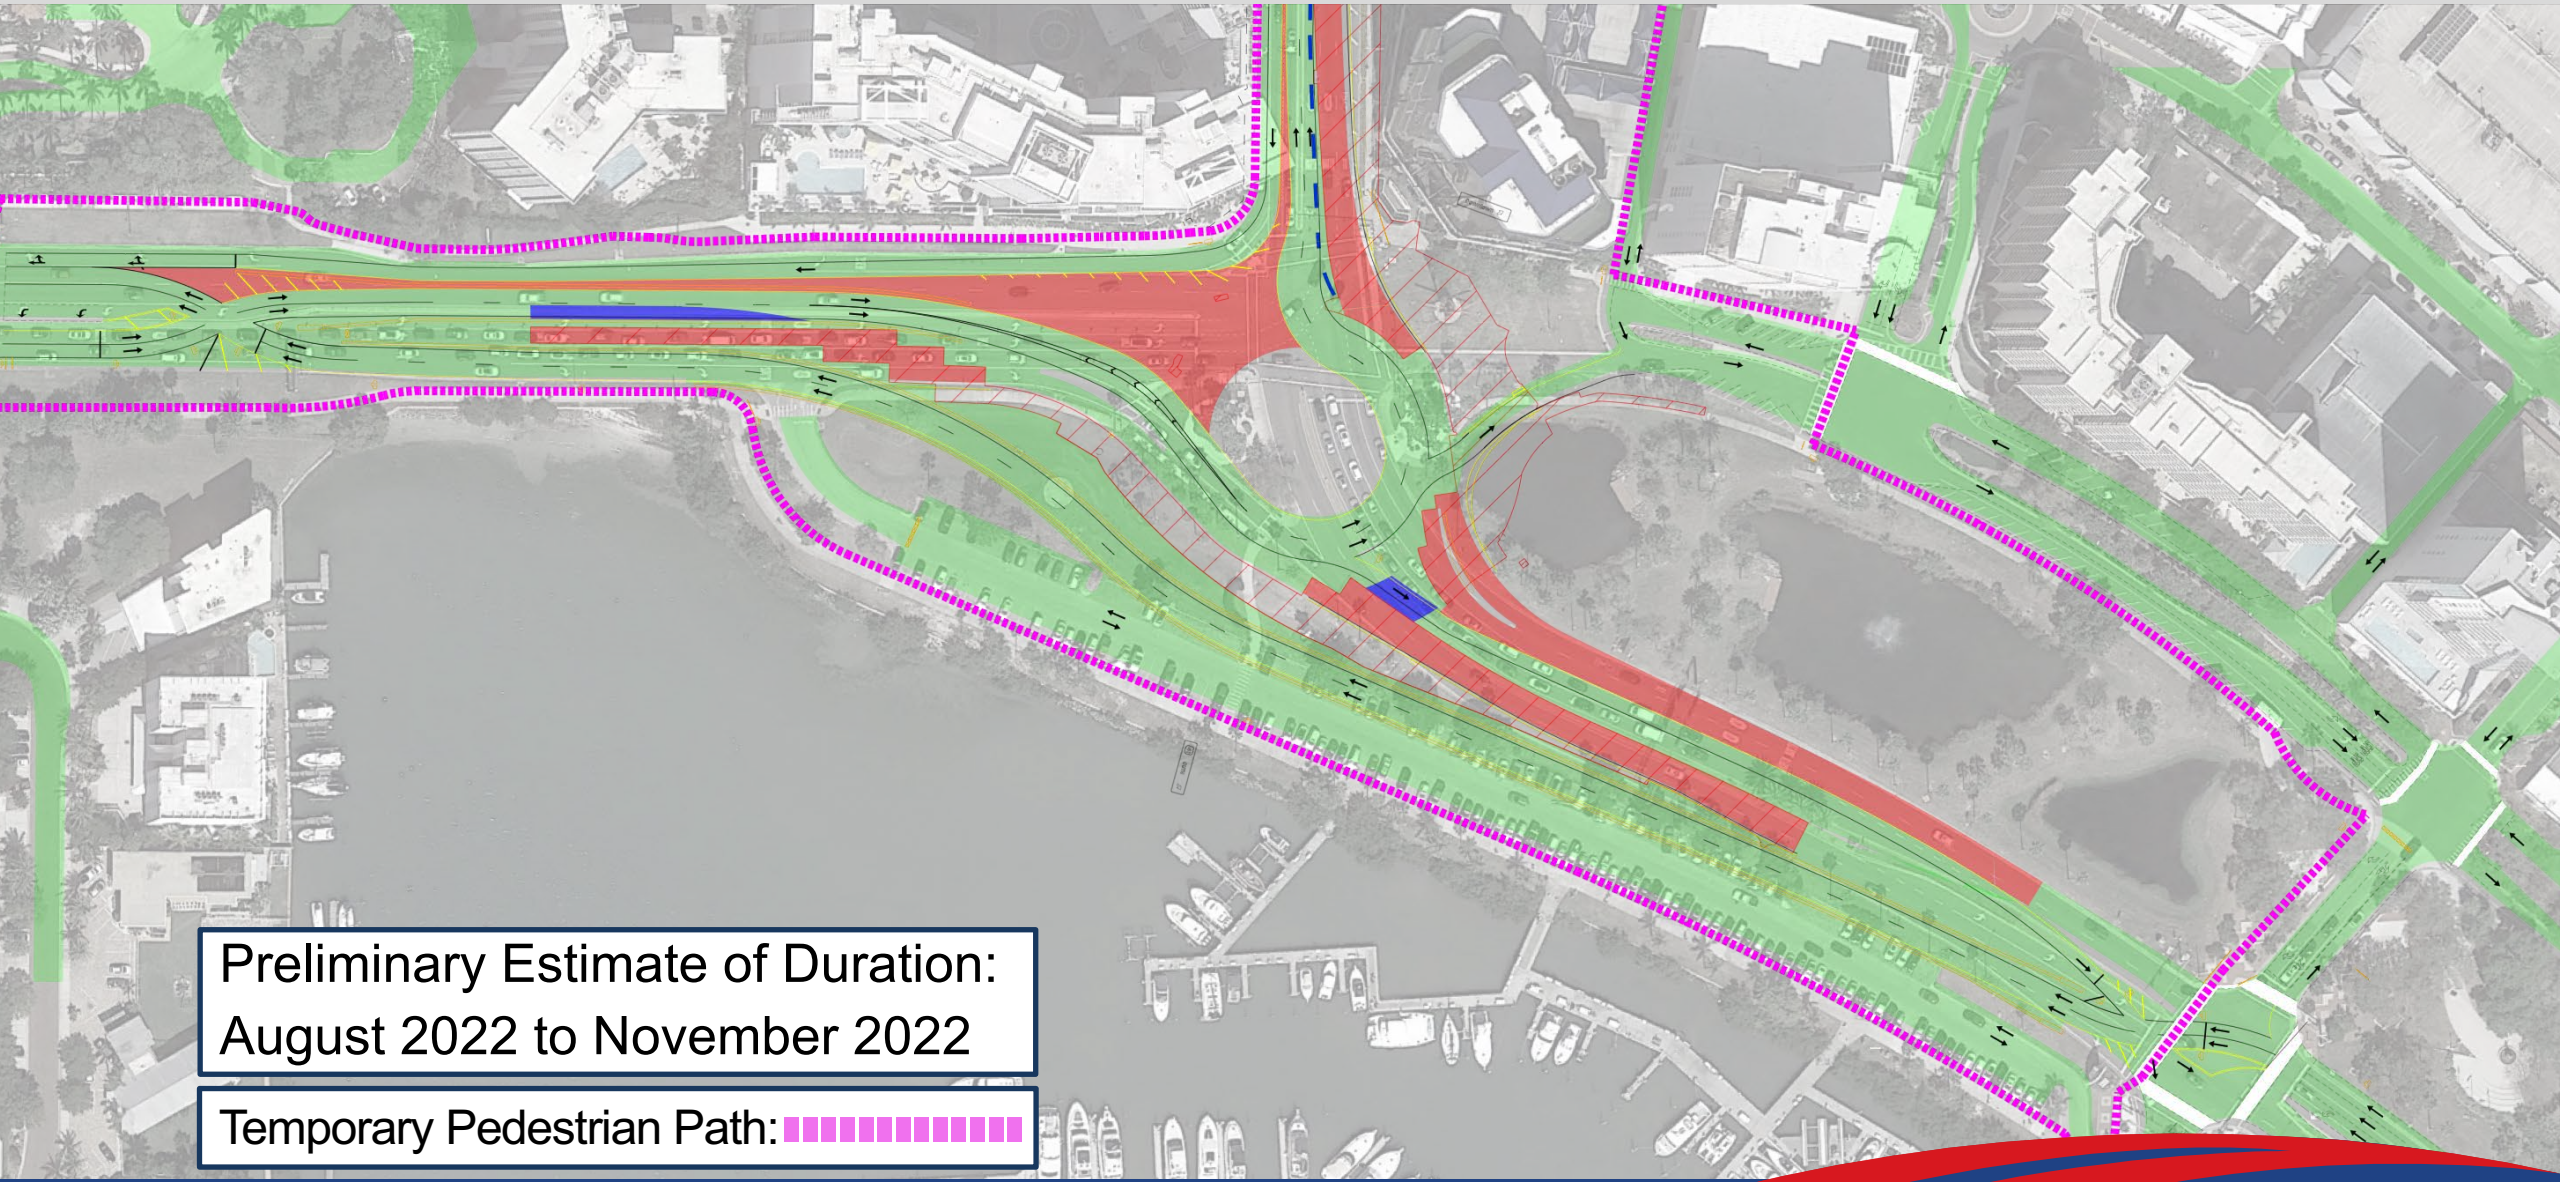

Preliminary Estimate of Duration:
August 2022 to November 2022

Temporary Pedestrian Path: 


Traffic Movements / Phase IIB

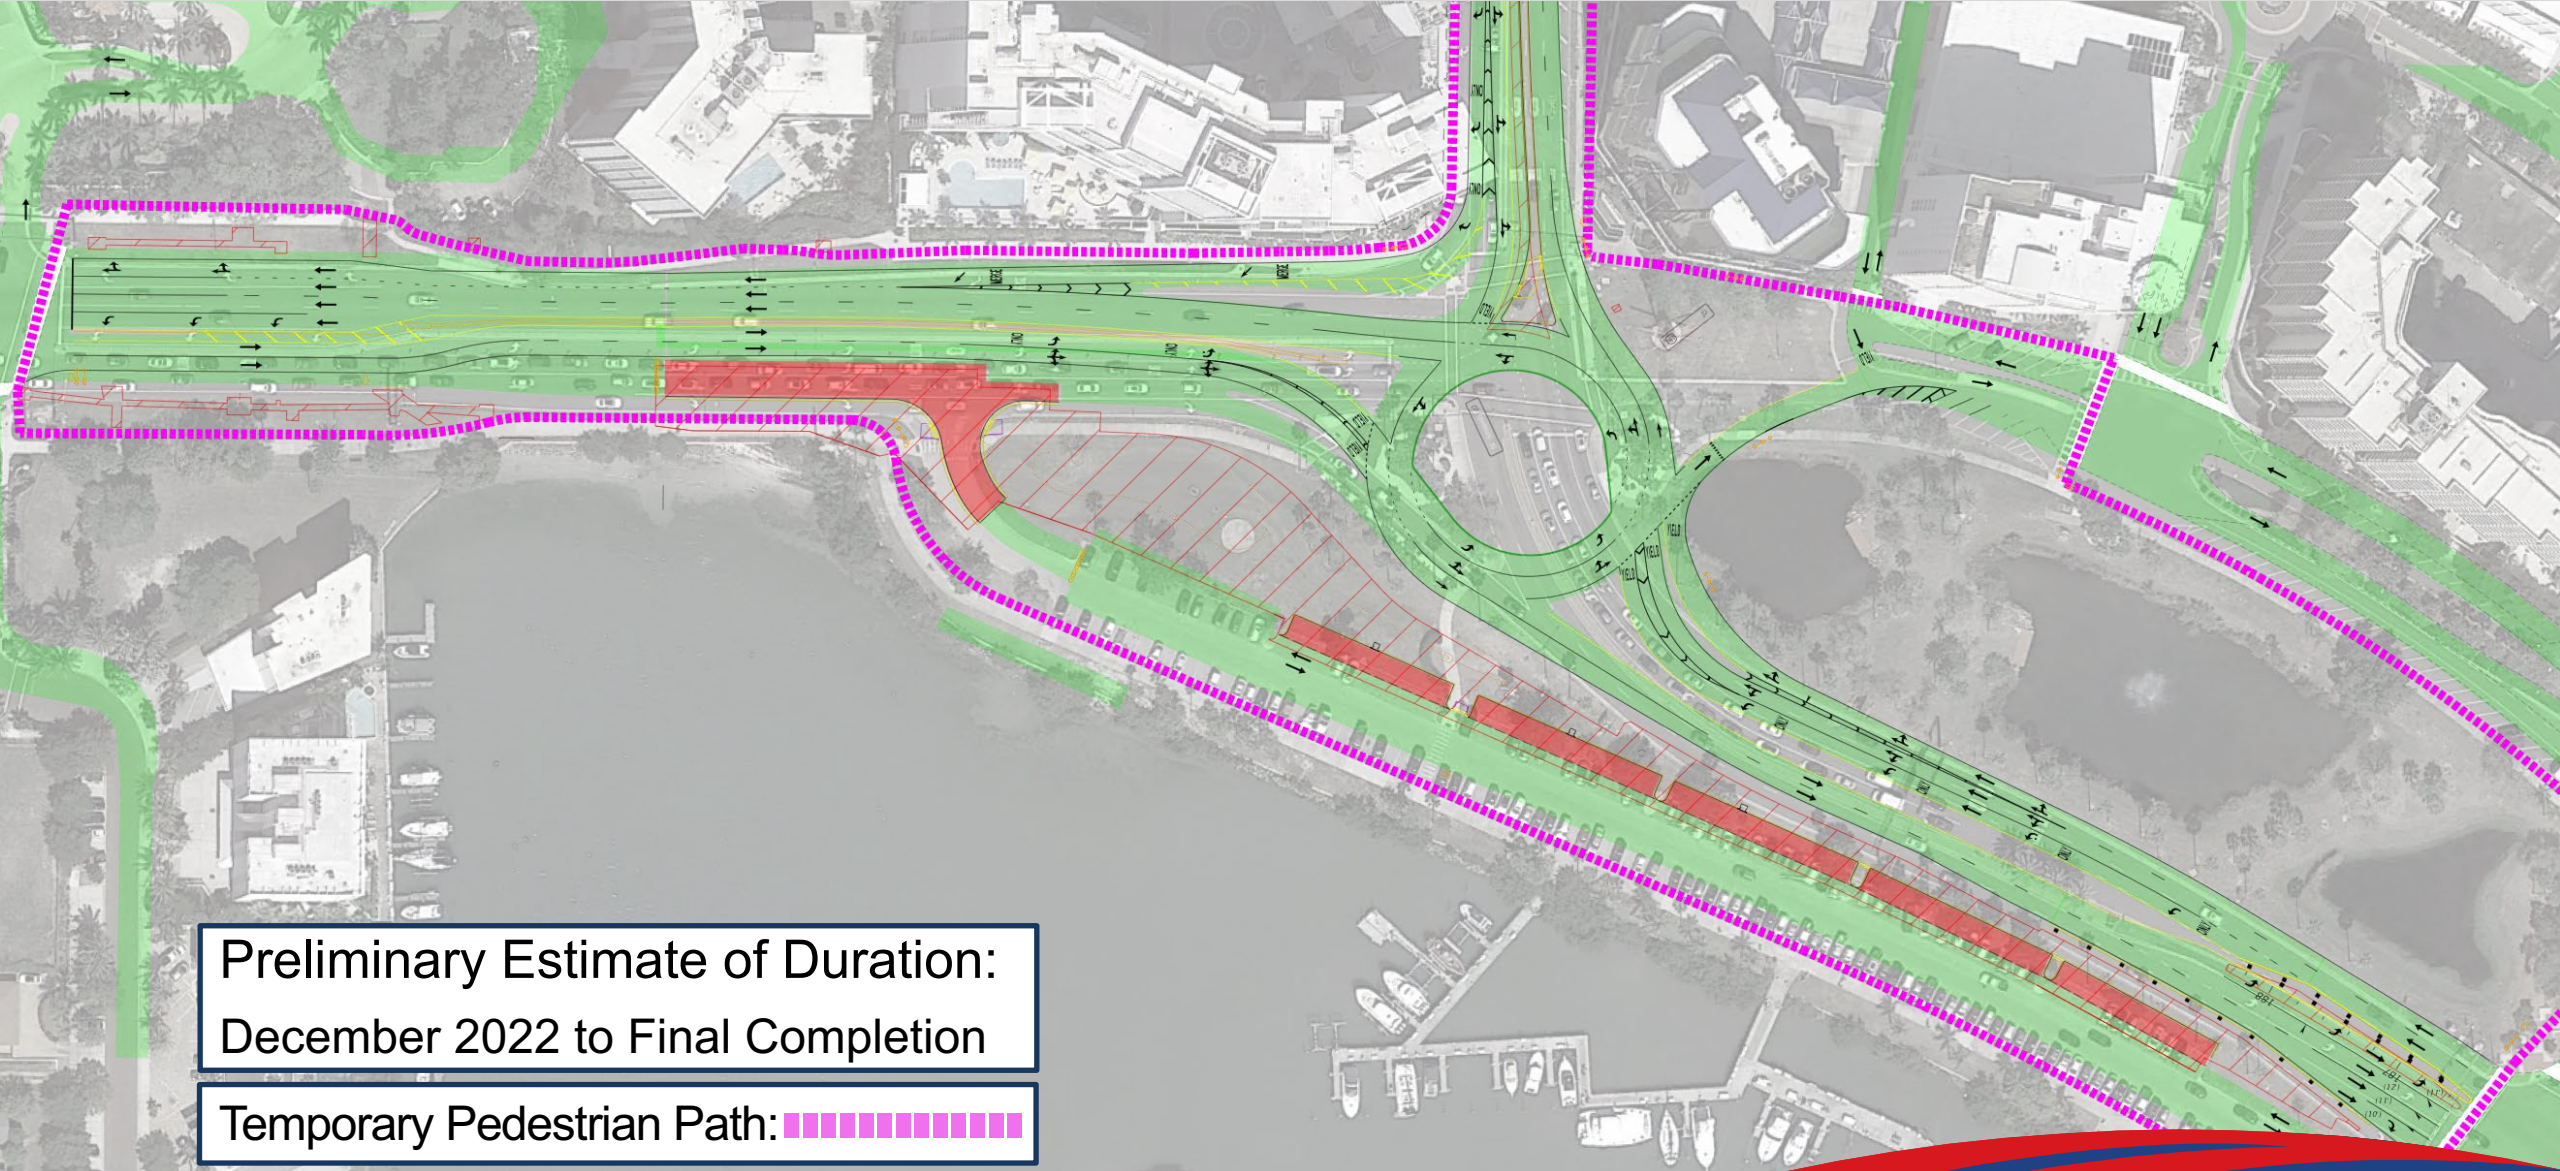

Preliminary Estimate of Duration:
December 2022 to Final Completion

Temporary Pedestrian Path: 

Temporary Pedestrian Route

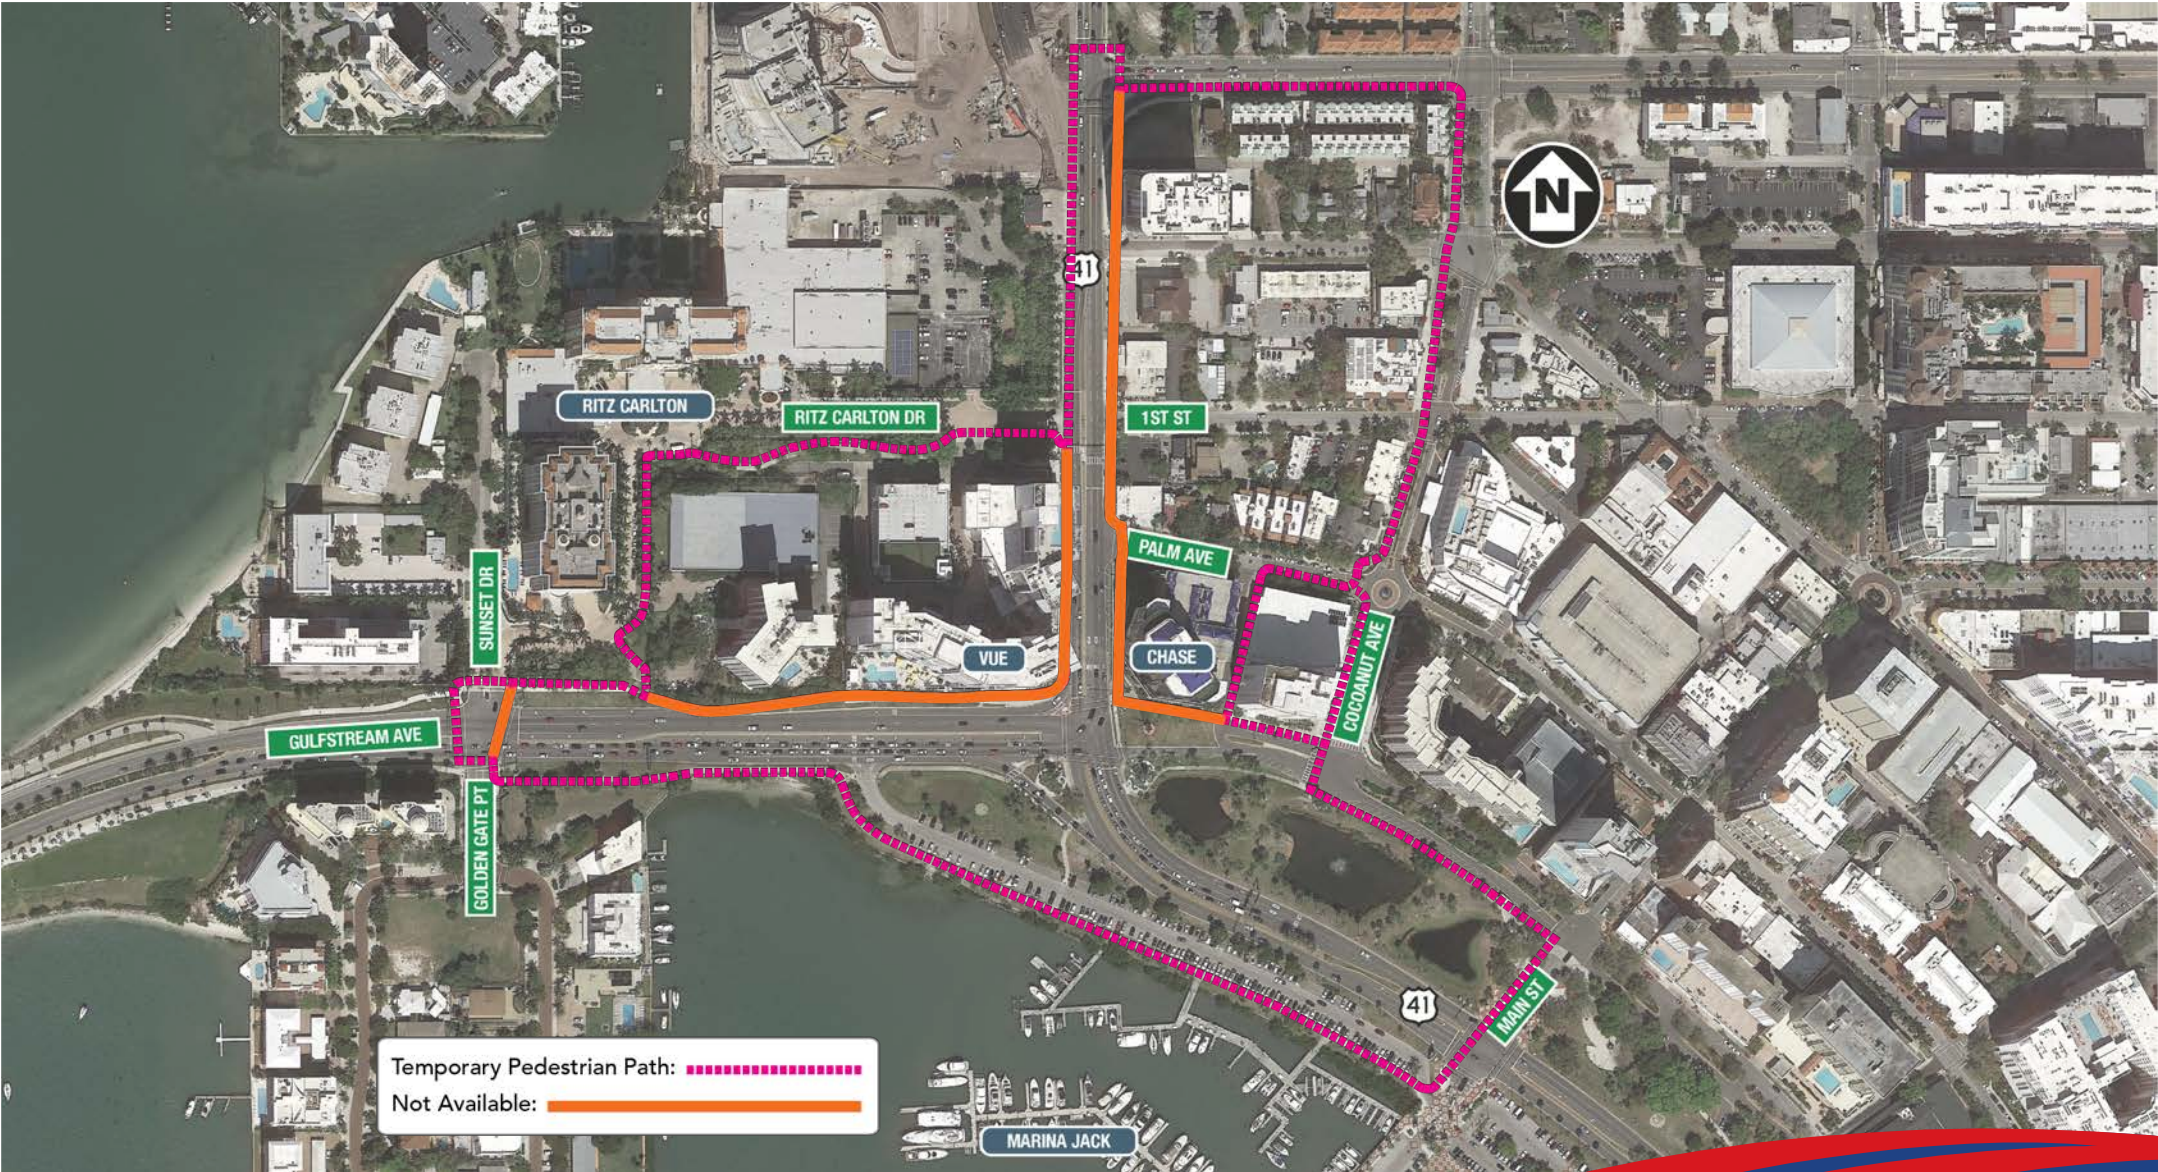

Final Rendering Overview



Final Rendering

